



Monthly Progress Report

February 2025

Cold Spring Harbor Central School District



Report prepared by Alex Unser





Table of Contents

Section I – Program Summary

Section II – Work Progress February 2025

Section III – Work Projected for March 2025

Section IV – Progress Photos

Section V – Monthly Workforce Summary - NA



Section I – Program Summary

February 2025

Project List

- Goose Hill PS Building Generator
- Westside Elementary School Kitchen & Bathroom Renovations
- Lloyd Harbor Elementary School Theatre Renovation
- Capital Improvement HVAC Upgrades
- HS/MS PAC Upgrades



Section II - Work Progress

February 2025

- **Phase III Goose Hill Building Generator**

- The factory startup with Cummins was unsuccessful due to gas pressure complications. Seaford and NAT Grid have been notified and are in the process of coming up with solutions.

- **Westside Elementary School Kitchen & Bathroom Renovations**

- Replacement doors were installed with all specified hardware.
- Completed the refinishing of the existing door frames.
- Replaced the damaged glass in the storeroom delivery door.
- Contractors continued the procurement of closeout documents.

- **Lloyd Harbor Elementary School Theatre Renovation**

- All Contractors have completed their respective punch lists.
 - The testing and balancing of the new HVAC systems was completed.
 - GC has completed painting the mechanical room ceiling.
 - Closeouts were requested from all contractors

- **Capital Improvement HVAC Upgrades**

- The Window Louver and fresh air ductwork installation was completed at Goose Hill.

- **HS/MS PAC Upgrades**

- Additional training and programming were conducted, some remains.
 - Completed the troubleshooting and repair of the edge lighting system.



Section III - Work Planned

March 2025

- **Phase III Goose Hill Building Generator**
 - To have the electrician and Cummins complete a successful factory start-up
- **Westside Elementary School Kitchen & Bathroom Renovations**
 - To receive all the closeout documents.
- **Lloyd Harbor Elementary School Theatre Renovation**
 - To receive all the closeout documentation.
- **Capital Improvement HVAC Upgrades**
 - To receive close-out documents from contractors who have completed their scope.
- **HS/MS PAC Upgrades**
 - To wrap up additional lighting program and training.
 - To close out all contractors.



Section IV – Progress Photos



Lloyd's UV's Trimmed and Panel Adjustments




Section IV – Progress Photos



Completed Steam Lines at Lloyd Crawlspace

Section IV – Progress Photos

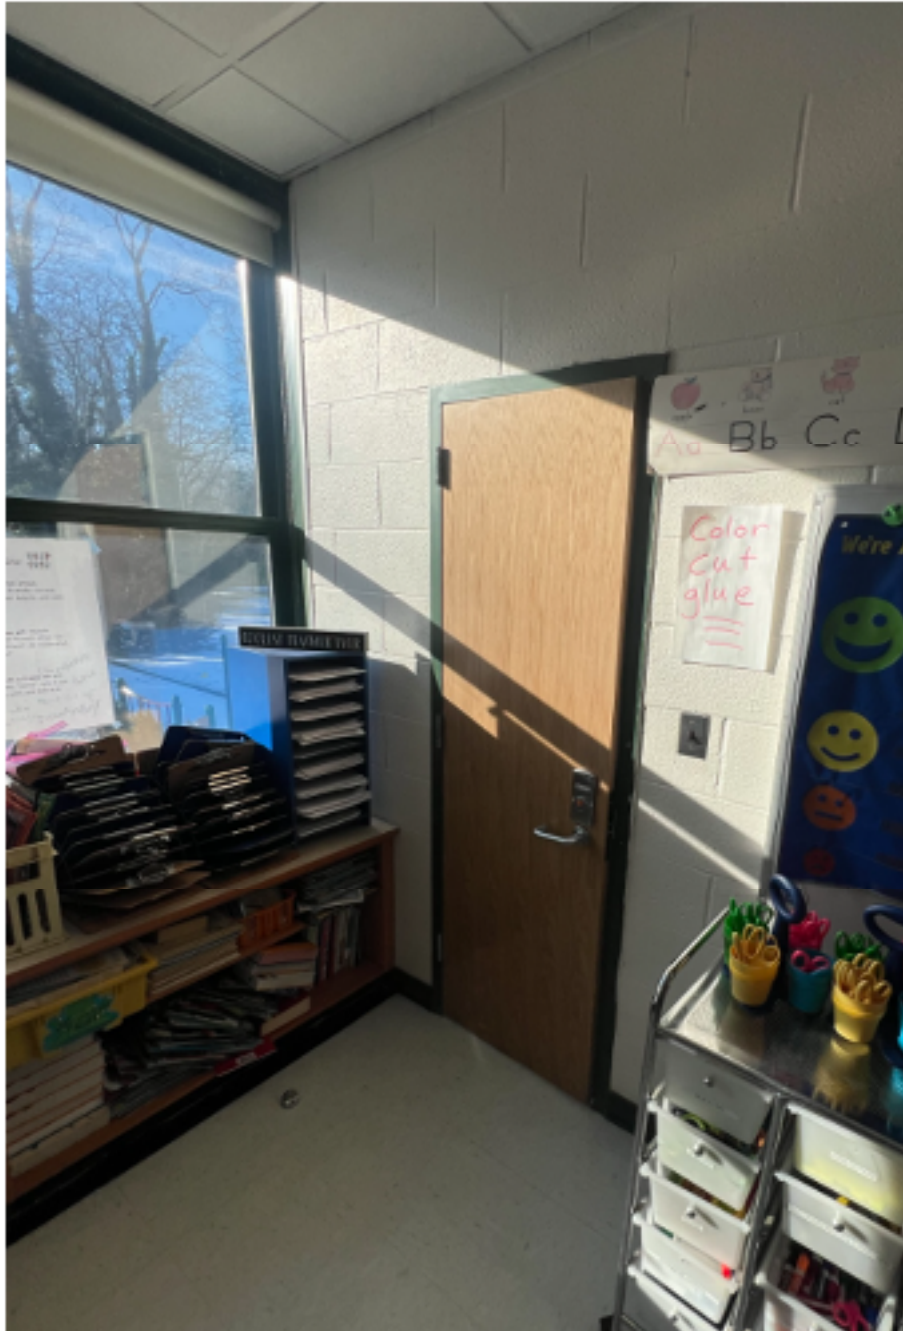

Newly Installed Doors for Westside Bathrooms



Cold Spring Harbor Central School District
February 2025

End of Progress Report
