



# Monthly Progress Report

March 2023

Cold Spring Harbor Central School District



Report prepared by Joseph Moisa







# Table of Contents

**Section I – Program Summary**

**Section II – Work Progress** March 2023

**Section III – Work Projected for** April 2023

**Section IV – Progress Photos**

**Section V – Monthly Workforce Summary**



## Section I – Program Summary

### March 2023

#### **Project List**

- Phase II Jr/Sr High School New Addition
- Phase IIA Jr/Sr High School STEM Wing
- GooseHill PS AP Room Upgrades
- GooseHill PS Phase III Building Generator



## Section II - Work Progress

### March 2023

- **Phase II Jr/Sr High School Addition**

- Continued the installation of the masonry block walls at the north and west exterior elevations.
- Completed the installation of the roof perimeter blocking.
- Started the installation of the roofing systems at all locations.
- Continued the installation of all underground domestic water, gas, and chemical waste piping.
- Continued the installation of the underground ductwork.
- Continued the installation of the overhead domestic water piping.
- Completed the installation of the storm water roof drainage piping.

- **Phase II Jr/Sr High School STEM Wing**

- Started the installation of the roof penetration curbs for the mechanical ductwork and steel dunnage.
- Started selective electrical demolition and investigative work.

- **GooseHill AP Room Upgrades**

- Completed the installation of roof top ductwork and duct stations.

- **Phase III GooseHill Building Generator**

- Continued the submission of preconstruction documents, shop drawings and product data.



## Section III - Work Planned

### April 2023

- **Phase II Jr/Sr High School Addition**

- Complete the installation of all underground domestic water, gas, and chemical waste piping.
- Complete the installation of the underground ductwork.
- Complete the installation of the exterior masonry block walls.
- Complete the installation of the roof systems.
- Continue the installation of the overhead domestic water piping.
- Start the installation of exterior brick at the courtyard walls.
- Start the installation of stone, vapor barrier and supplemental steel for the concrete slabs.
- Complete finish landscaping and hydroseeding at the site work areas on the north and east sides of the existing building.
- Complete the site sanitary and storm drainage piping connections to tie in the systems.

- **Phase II Jr/Sr High School STEM Wing**

- Complete the installation of the roof penetration curbs for the mechanical ductwork and steel dunnage.
- Continue selective electrical demolition and investigative work on night shift.

- **GooseHill AP Room Upgrades**

- Complete the installation of spiral ductwork and wall enclosure.
- Fabricate structural steel for the dunnage.
- Continue the electrical rough in for the new roof top unit.



- **Phase III GooseHill Building Generator**
  - Continue the submission of preconstruction documents, shop drawings and product data.



## Section IV – Progress Photos



Jr/Sr HS New Addition Roofing Installation





## Section IV – Progress Photos



Jr/Sr HS New Addition Roofing Installation



## Section IV – Progress Photos



Jr/Sr HS New Addition Sloped Roofing Installation





## Section IV – Progress Photos



Jr/Sr HS New Addition Masonry Block Walls

## Section IV – Progress Photos



Jr/Sr HS New Addition Masonry Walls





## Section IV – Progress Photos



Jr/Sr HS New Addition Masonry Walls



## Section IV – Progress Photos



Jr/Sr HS New Addition Storm Water Drainage Piping





## Section IV – Progress Photos



Jr/Sr HS New Addition Acid Waste Piping



## Section IV – Progress Photos



Jr/Sr HS New Addition Overhead Domestic Water Piping





## Section IV – Progress Photos

d



GooseHill PS AP Room Ductwork




## Section V – Workforce Summary – Company/Hours

Phase II Jr/Sr High School New Addition & Fitness Center

March 2023

### Daily Log Manpower Report

#### ▼ MANPOWER GRAPH

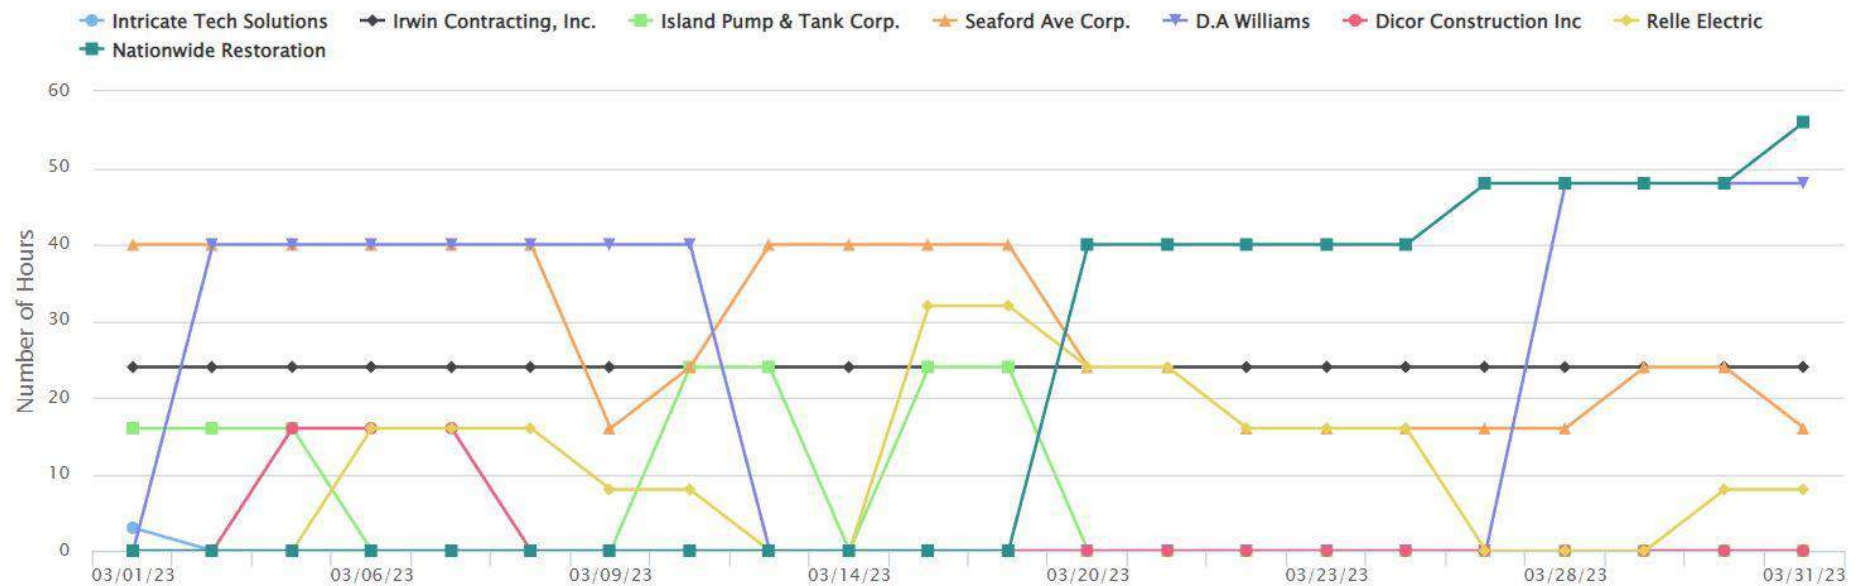



Cold Spring Harbor Central School District  
March 2023

**End of Progress Report**
