



Monthly Progress Report

October 2022

Cold Spring Harbor Central School District



Report prepared by Joseph Moisa







Table of Contents

Section I – Program Summary

Section II – Work Progress **October 2022**

Section III – Work Projected for **November 2022**

Section IV – Progress Photos

Section V – Monthly Workforce Summary



Section I – Program Summary October 2022

Project List

- Phase II Jr/Sr High School New Addition
- Phase II Jr/Sr High School Fitness center



Section II - Work Progress

October 2022

- **Phase II Jr/Sr High School Addition**

- Continued excavations, forms and pouring concrete for the foundation footings and foundation walls at the northwest corner and south elevation of the new building addition.
- Continued structural steel member fabrications off site.
- Installed the RPZ hot box assemblies.
- Completed the startup of the new fuel oil transfer pumps and oil tank systems for boiler rooms #2, #3, and field house.
- Installed electrical transformer and panel in the fitness center electrical closet.
- Received electrical transformer for the main electrical room new addition service.
- Began importing fill to bring up grade and backfill foundation.
- Installed the wiring in the roof top conduits for the new addition electrical service running from the main distribution panel to the fitness center electrical closet.

- **Phase II Jr/Sr High School Fitness Center**

- Completed door hardware.



Section III - Work Planned November 2022

- **Phase II Jr/Sr High School Addition**
 - Complete excavations, forms and pouring concrete for the foundation footings, foundation walls and piers.
 - Start excavation and installation of underground plumbing and mechanical ductwork.
 - Complete structural steel member fabrications and painting off site.
 - Continue importing fill to bring up grade and backfill foundation.

- **Phase II Jr/Sr High School Fitness Center**
 - Complete finish painting and touch ups.
 - Complete punch list items.



Section IV – Progress Photos



Jr/Sr HS New Addition Foundation Wall Footings



Section IV – Progress Photos



Jr/Sr HS New Addition Foundation Work



Section IV – Progress Photos



Jr/Sr HS New Addition Foundation Walls



Section IV – Progress Photos



Jr/Sr HS Foundation Piers

Section IV – Progress Photos



Jr/Sr HS New RPZ and Hot box Installations



Section IV – Progress Photos



Jr/Sr HS New Addition Electric Service Wiring



Section IV – Progress Photos



Jr/Sr HS Fitness Center Electrical Transformer and Panel



Section IV – Progress Photos



Jr/Sr HS Main Electrical Room Transformer




Section V – Workforce Summary – Company/Hours

Phase II Jr/Sr High School New Addition & Fitness Center

October 2022

▼ MANPOWER GRAPH

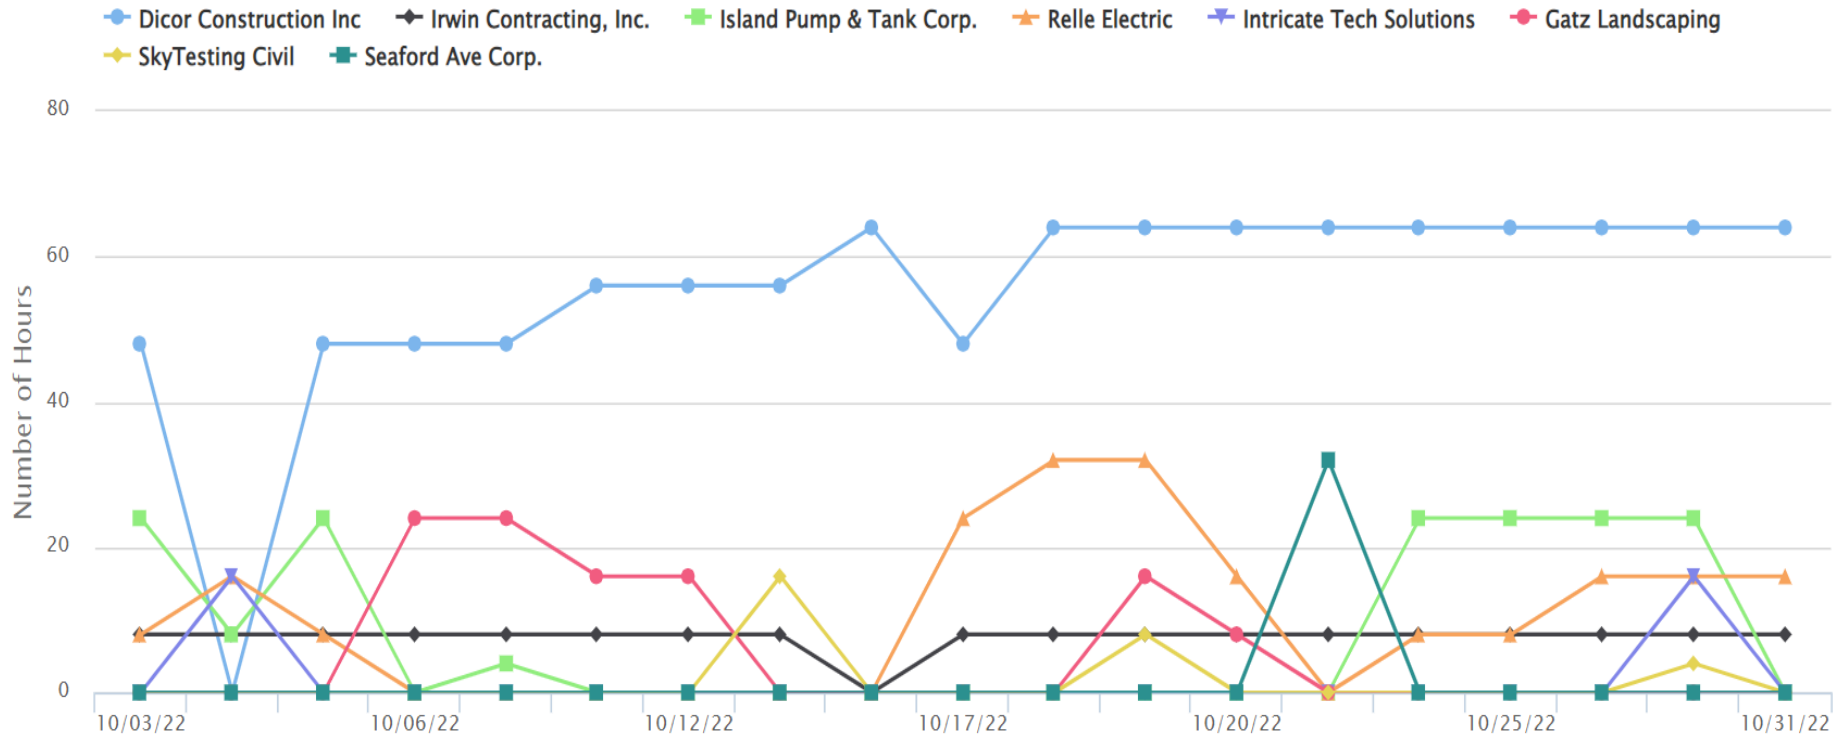



Cold Spring Harbor Central School District
October 2022

End of Progress Report
